

June 2021 Construction Update

Construction began on the Dayton Parkway Interchange project in the beginning of May 2020. The work on the new diverging diamond interchange is being performed by C.S. McCrossan based out of Maple Grove. Explore the project's website for more background on the project: www.daytonparkwayinterchange.com

MnDOT's work on I-94 from Maple Grove to Clearwater also began in Spring of 2020. More information on the I-94 work can be found on MnDOT's website: www.dot.state.mn.us/i94-mg-clearwater/index.html. Sign-up for the I-94 project updates from the following link: [Subscribe Here](#)

1. Dayton Parkway Construction Progress

- a. Bridge Construction
 - i. Bridge work nears completion as approach panels and concrete barriers were constructed.
 - ii. Paint crews have been painting portions of the bridge and will continue their work through the summer.



A view of the Dayton Parkway bridge beams over I-94 from the west abutment looking to the east.




A view from I-94 below the newly erected Dayton Parkway bridge beams.

- b. Roadway Construction
 - i. Underground utility work continues the new Dayton Parkway on both side of I-94. Grading crews follow and the roadway is beginning to take shape.
 - ii. The Holly Lane/Territorial Intersection was closed to traffic as of June 28th. The intersection will remain closed as the new Dayton Parkway is constructed in the area and new intersections are constructed.
 - iii. Construction is on schedule and set to be substantially complete by the end of 2021.



A view looking down the future Dayton Parkway from the Brockton Lane intersection.

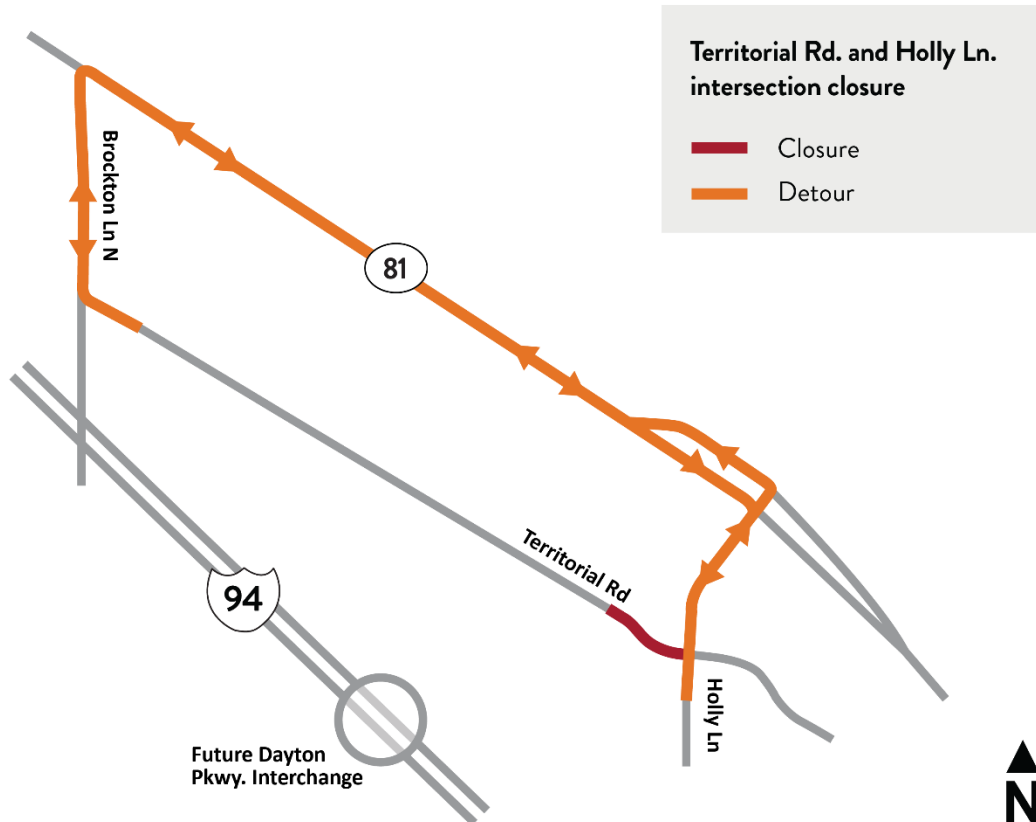

An overview of the Territorial Rd Detour route. Closure will be in place June 28th through August 31st

2. Traffic Control/Detours

- a. Visit MnDOT's website to sign up for updates on lane and ramp closures along I-94 in the vicinity of the Dayton Parkway Interchange: www.dot.state.mn.us/i94-mg-clearwater/index.html
- b. Territorial Road is closed at Holly Lane as of June 28th. The closure will remain through the end of August. Detour route is County Road 81 to Brockton Lane to Territorial Road

3. Construction and Traffic Look Ahead

- a. Bridge Construction
 - i. Final pieces of the bridge will be constructed, aesthetic elements will be added, and bridge painting will continue through the summer.
 - ii. Completion of the bridge is estimated for this summer.
- b. Roadway Construction
 - i. Underground utility work and grading on the interchange ramps and new Dayton Parkway.
 - ii. Curbs follow behind the grading work.

CONSTRUCTION UPDATES

c. Traffic

- i. As part of the MnDOT I-94 Design Build project, WB I-94 lanes remain separated between the I-94/494/694 interchange and HWY 241. Visit the MnDOT link above for details.
- ii. The Territorial Road closure will remain in place through the end of August.

4. Other

a. COVID-19 Jobsite Protections

- i. While the construction of the new Dayton Parkway Interchange is exciting and will drastically change the landscape of this area, the City of Dayton is requesting the outside public avoids contact with the job site and construction personnel in order to protect the health, safety and welfare of the project's workforce and public during the COVID-19 outbreak.
- ii. Please contact the personnel listed below if you have any questions about the project. Thank you for your cooperation!



Please be alert and careful driving through construction work zones.
