

July 2021 Construction Update

Construction began on the Dayton Parkway Interchange project in the beginning of May 2020. The work on the new diverging diamond interchange is being performed by C.S. McCrossan based out of Maple Grove. Explore the project's website for more background on the project: www.daytonparkwayinterchange.com

MnDOT's work on I-94 from Maple Grove to Clearwater also began in Spring of 2020. More information on the I-94 work can be found on MnDOT's website: www.dot.state.mn.us/i94-mg-clearwater/index.html. Sign-up for the I-94 project updates from the following link: [Subscribe Here](#)

1. Dayton Parkway Construction Progress

- a. Roadway Construction
 - i. The Holly Lane/Territorial Intersection was closed to traffic as of June 28th. The intersection will remain closed as the new Dayton Parkway is constructed in the area and new intersections are constructed.
 - ii. Curb and gutter have been installed between the bridge and Holly Ln as the parkway continues to take shape.



A view from the new Dayton Parkway bridge looking down onto the I-94 design-build project below.




A view of the new Dayton Parkway looking east towards CR 81 as construction of the parkway progresses.

- iii. Landscape elements like stone retaining walls are in the process of being constructed.
 - iv. Construction is on schedule and set to be substantially complete by the end of 2021.
- b. Bridge Construction
- i. Bridge work is mostly complete. In June, crews poured concrete median barrier across the bridge.
 - ii. Final touches on the bridge work will continue through the summer.



A view looking down the future Dayton Parkway from the Brockton Lane intersection.

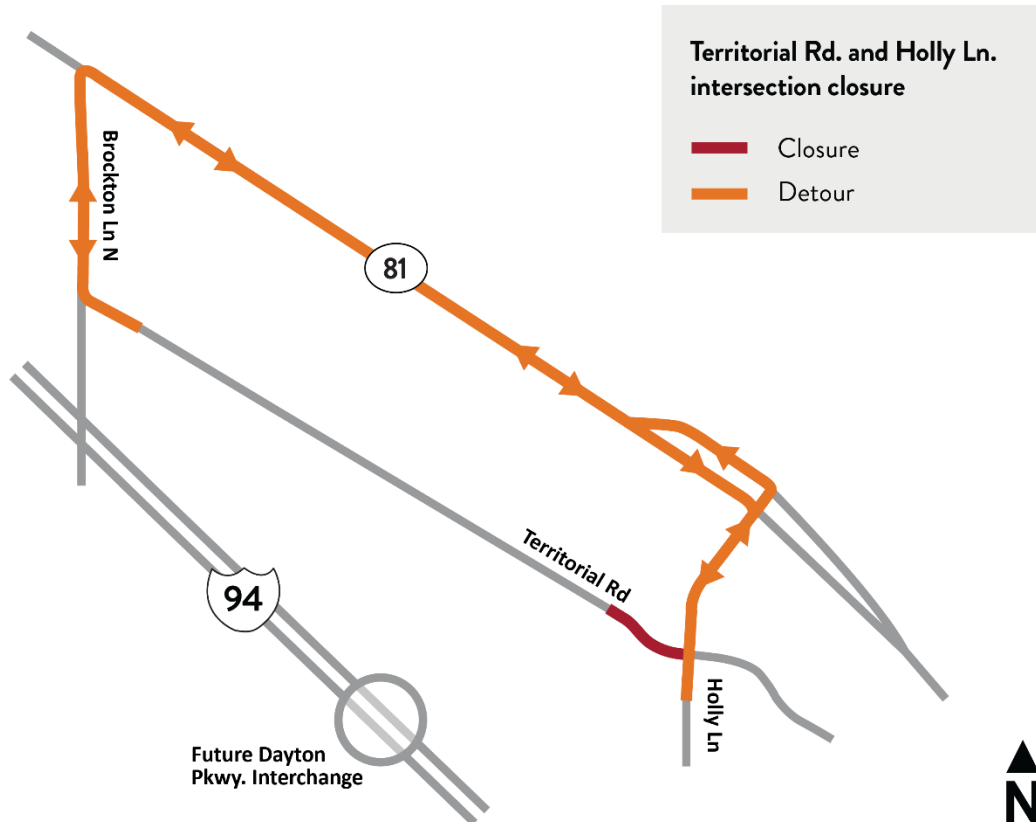

An overview of the Territorial Rd Detour route. Closure will be in place June 28th through August 31st

2. Traffic Control/Detours

- Visit MnDOT’s website to sign up for updates on lane and ramp closures along I-94 in the vicinity of the Dayton Parkway Interchange: www.dot.state.mn.us/i94-mg-clearwater/index.html
- Territorial Road is closed at Holly Lane as of June 28th. The closure will remain through the end of August. Detour route is County Road 81 to Brockton Lane to Territorial Road

3. Construction and Traffic Look Ahead

- Bridge Construction
 - Final pieces of the bridge will be constructed, aesthetic elements will be added, and bridge painting will continue through the summer.
 - Completion of the bridge is estimated for this summer.
- Roadway Construction
 - Final grading on the interchange ramps and new Dayton Parkway. Curbs follow behind the grading work.
 - Road paving and trail paving are scheduled to begin later this summer/early fall.

CONSTRUCTION UPDATES

c. Traffic

- i. As part of the MnDOT I-94 Design Build project, WB I-94 lanes remain separated between the I-94/494/694 interchange and HWY 241. Visit the MnDOT link above for details.
- ii. The Territorial Road closure will remain in place through the end of August.

4. Other

a. COVID-19 Jobsite Protections

- i. While the construction of the new Dayton Parkway Interchange is exciting and will drastically change the landscape of this area, the City of Dayton is requesting the outside public avoids contact with the job site and construction personnel in order to protect the health, safety and welfare of the project's workforce and public during the COVID-19 outbreak.
- ii. Please contact the personnel listed below if you have any questions about the project. Thank you for your cooperation!



Please be alert and careful driving through construction work zones.
